



**BATCH # 1 PAVING
&
DRAINAGE IMPROVEMENTS
PROJECT**

HARRIS COUNTY, TEXAS

Weekly Progress Report

HDR| Engineering Inc.

Project No.12-022

**Week Ending
January 11, 2014**

Submitted to

Piney Point City Council

HDR | ONE COMPANY
Many Solutions[®]
4635 Southwest Freeway, Houston TX 77027-7169
(713) 622-9264. Fax (713) 622-9265. www.hdr.com

December 29, 2013 to January 11, 2014
Activity/Status

Batch # 1 Paving & Drainage
IMPROVEMENTS

MOBILIZATION:

- This period no work was performed on this aspect of the project.

PAVING ITEMS:

JAMESTOWN ROAD

- This period no work was performed on this aspect of the project.

CALICO LANE

- This period no work was performed on this aspect of the project.

JAN KELLY LANE

- This period no work was performed on this aspect of the project.

GINGHAM DRIVE

- This period no work was performed on this aspect of the project.

GREEN OAK DRIVE

- This period no work was performed on this aspect of the project at this time.

DRAINAGE ITEMS: AAA Paving

JAMESTOWN ROAD

- This period no work was performed on this aspect of the project at this time


CALICO LANE

- This period no work was performed on this aspect of the project.

December 29, 2013 to January 11, 2014
Activity/Status

Batch # 1 Paving & Drainage
IMPROVEMENTS

DRAINAGE ITEMS: AAA Paving (cont.)

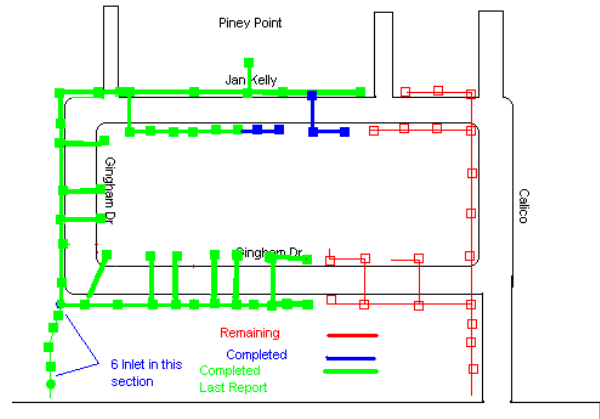

Drawing of the storm lines for Jan Kelly, Calico and Gingham area. Blue is completed this period; Green past weeks and red is still remaining to be done.

JAN KELLY LANE

- Completed placement of the 18-inch & 24-inch storm sewer along the east side of Jan Kelly that flows to the south, up to 470 Jan Kelly.
- Installed new inlets along the east side of Jan Kelly on lines flowing south in front of 466 and 470 Jan Kelly.
- Raised the inlet grate at Bending Oaks and Jan Kelly northwest corner.

GINGHAM DRIVE

- Continue maintaining temporary driveways.

[December 29, 2013 to January 11, 2014
Activity/Status](#)

**Batch # 1 Paving & Drainage
IMPROVEMENTS**

**GREEN OAK DRIVE/HABERSHAM
DITCH OUTFALL**

- This period no work was performed on this aspect of the project at this time

WATER ITEMS :

JAMESTOWN ROAD

- This period no work was performed on this aspect of the project.

CALICO LANE

- This period no work was performed on this aspect of the project.
- This period no work was performed on this aspect of the project.

GINGHAM DRIVE

- None required

**GREEN OAK DRIVE/HABERSHAM
DITCH OUTFALL**

- None required

TREE PROTECTION:

JAMESTOWN ROAD

- This period no work was performed on this aspect of the project.

CALICO LANE

- This period no work was performed on this aspect of the project.

[December 29, 2013 to January 11, 2014
Activity/Status](#)

**Batch # 1 Paving & Drainage
IMPROVEMENTS**

TREE PROTECTION: (cont.)

JAN KELLY LANE

- This period no work was performed on this aspect of the project at this time

GINGHAM DRIVE

- This period no work was performed on this aspect of the project.



Contractor installed the wooden fence between Piney Point and Gingham at 439 Piney Point. View to the east.



Contractor installed the wooden fence between Piney Point and Gingham at 443 Piney Point. View to the southeast.

[December 29, 2013 to January 11, 2014
Activity/Status](#)

**Batch # 1 Paving & Drainage
IMPROVEMENTS**

**GREEN OAK DRIVE/HABERSHAM
DITCH OUTFALL**

- Completed

SUPPLEMENTAL ITEMS:

JAMESTOWN ROAD

- This period no work was performed on this aspect of the project.

CALICO LANE

- This period no work was performed on this aspect of the project.

JAN KELLY LANE

- Lowered and installed a new long sewer service line for 467 & 470 Jan Kelly, it was in the way of placement of the new storm line.
- Installed new yard drain connection at 470 & 510 Jan Kelly.

GINGHAM DRIVE

- Completed replacement of the existing wooden fencing in the easement between 439 Piney Point and Gingham.
- Replaced the sprinkler system in the back yard of 439 Piney Point.
- Placed sod grass in the back yard of 439 Piney Point.
- Initiated excavation for the metal fence post at 430 Gingham.

[December 29, 2013 to January 11, 2014
Activity/Status](#)

**Batch # 1 Paving & Drainage
IMPROVEMENTS**

**GREEN OAK DRIVE/HABERSHAM
DITCH OUTFALL**

- Completed



Re-installing the metal fence at 439 Piney Point View to the west.



The contractor is completing installation of the wooden back fence in the easement between Piney Point Rd and Gingham. View to the east. Installed sod grass in the back yard of 439 Piney Point.

Piney Point Batch # 1 Paving & Drainage
Improvements Project Progress Report for
Week ending January 11, 2013

Notes:

Job was closed Wednesday January 1, 2014 for
New Years day.

Monday January 6, 2014 was unable to install
storm sewer piping due to cold weather. It was
too cold to mix the stabilized sand.

Tuesday was unable to start installing storm
sewer pipe till 11:30 due no stabilized sand
because of the cold weather.

Thursday January 9, 2014 the job site was Rain
out.

Next Week's Planned Activities
January 12, 2014 to January 18, 2014

Batch # 1 Paving & Drainage
IMPROVEMENTS

MOBILIZATION:

- This period no work was performed on this aspect of the project.



Contractor placed the sod grass in the easement between Piney Point Rd and Gingham on the south side of the fence. View to the east.

PAVING ITEMS: AAA Paving

JAMESTOWN ROAD

- This period no work was is planned on this aspect of the project.

CALICO LANE

- This period no work is planned on this aspect of the project.

JAN KELLY LANE

- This period no work is planned on this aspect of the project.

GINGHAM DRIVE

- This period no work is planned on this aspect of the project.

Next Week's Planned Activities
January 12, 2014 to January 18, 2014

Batch # 1 Paving & Drainage
IMPROVEMENTS

GREEN OAK DRIVE

- This period no work is planned on this aspect of the project.

DRAINAGE ITEMS: AAA Paving

JAMESTOWN ROAD

- This period no work is planned on this aspect of the project.

CALICO LANE

- Continue placement of the new 24-inch storm sewer line.



Contractor placed the sod grass in the easement between Piney Point Rd and Gingham on the north side of the fence. View to the west.

JAN KELLY LANE

- This period no work is planned on this aspect of the project.

[Next Week's Planned Activities \(cont.\)
January 12, 2014 to January 18, 2014](#)

**Batch # 1 Paving & Drainage
IMPROVEMENTS**

DRAINAGE ITEMS: AAA Paving (cont.)

GINGHAM DRIVE

- This period no work is planned on this aspect of the project.

**GREEN OAK DRIVE/HABERSHAM
DITCH OUTFALL**

- Completed

WATER ITEMS:

JAMESTOWN ROAD

- This period no work is planned on this aspect of the project.

CALICO LANE

- This period no work is planned on this aspect of the project.

JAN KELLY LANE

- Completed

GINGHAM DRIVE

- This period no work is planned on this aspect of the project.

**GREEN OAK DRIVE/HABERSHAM
DITCH OUTFALL**

- This period no work is planned on this aspect of the project.

[Next Week's Planned Activities \(cont.\)
January 12, 2014 to January 18, 2014](#)

**Batch # 1 Paving & Drainage
IMPROVEMENTS**

TREE PROTECTION:

JAMESTOWN ROAD

- This period no work is planned on this aspect of the project.

CALICO LANE

- This period no work is planned on this aspect of the project.

JAN KELLY LANE

- This period no work is planned on this aspect of the project.

GINGHAM DRIVE

- This period no work is planned on this aspect of the project.

TREE PROTECTION: (cont.)

**GREEN OAK DRIVE/HABERSHAM
DITCH OUTFALL**

- This period no work is planned on this aspect of the project.

SUPPLEMENTAL ITEMS:

JAMESTOWN ROAD

- This period no work is planned on this aspect of the project.

CALICO LANE

- This period no work is planned on this aspect of the project.

Next Week's Planned Activities (cont.)
January 12, 2014 to January 18, 2014

Batch # 1 Paving & Drainage
IMPROVEMENTS

SUPPLEMENTAL ITEMS: (cont.)

JAN KELLY LANE

- This period no work is planned on this aspect of the project.

GINGHAM DRIVE

- This period no work is planned on this aspect of the project.

GREEN OAK DRIVE/HABERSHAM
DITCH OUTFALL

- This period no work is planned on this aspect of the project.



Contractor marked out the location of the new storm sewer line location on Calico Lane and Piney Point road.



Contractor had to lower a sanitary sewer service to install the new storm sewer piping. View to the east.
