



**BATCH # 1 PAVING
&
DRAINAGE IMPROVEMENTS
PROJECT**

HARRIS COUNTY, TEXAS

Weekly Progress Report

**HDR| Engineering Inc.
Project No.12-022**

**Week Ending
January 25, 2014**

Submitted to

Piney Point City Council

HDR | ONE COMPANY
Many Solutions®
4635 Southwest Freeway, Houston TX 77027-7169
(713) 622-9264. Fax (713) 622-9265. www.hdr.com

January 19, 2014 to January 25, 2014
Activity/Status

Batch # 1 Paving & Drainage
IMPROVEMENTS

MOBILIZATION:

- This period no work was performed on this aspect of the project.

PAVING ITEMS:

JAMESTOWN ROAD

- This period no work was performed on this aspect of the project.

CALICO LANE

- This period no work was performed on this aspect of the project.

JAN KELLY LANE

- This period no work was performed on this aspect of the project.

GINGHAM DRIVE

- This period no work was performed on this aspect of the project.

GREEN OAK DRIVE

- This period no work was performed on this aspect of the project at this time.

DRAINAGE ITEMS: AAA Paving

JAMESTOWN ROAD

- This period no work was performed on this aspect of the project at this time

CALICO LANE

- Continue Removal of the old storm sewer piping Gingham Dr. toward Jan Kelly.


January 19, 2014 to January 25, 2014
Activity/Status

Batch # 1 Paving & Drainage
IMPROVEMENTS

DRAINAGE ITEMS: AAA Paving (cont.)

CALICO LANE (cont.)

- Continue Installation of the new 24-inch HDPE/RCP storm piping and inlets from Gingham Dr. toward Jan Kelly.

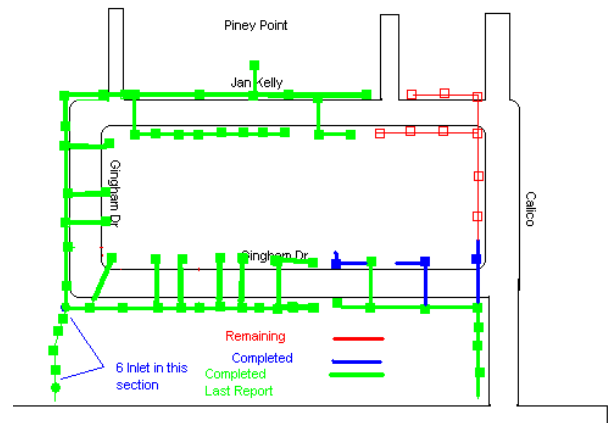

Drawing of the storm lines for Jan Kelly, Calico and Gingham area. Blue is completed this period; Green past weeks and red is still remaining to be done.

JAN KELLY LANE

- Initiated the clean up and redressing the street shoulders. Cutting to grade.

GINGHAM DRIVE

- Completed installation of the 24-inch and 18-inch storm sewer line with inlets from Calico south on Gingham. 100% completed with storm sewer pipe installation on Gingham.
- Reconnected yard drains for 11425 Calico, 510, 509 Gingham and 475 Gingham Dr.
- Continued with clean up and redressing the street shoulders.

January 19, 2014 to January 25, 2014
Activity/Status

Batch # 1 Paving & Drainage
IMPROVEMENTS

GREEN OAK DRIVE/HABERSHAM
DITCH OUTFALL

- This period no work was performed on this aspect of the project at this time

WATER ITEMS :

JAMESTOWN ROAD

- AAA sub-contractor excavated and installed the 30-foot water line by-pass on Tynebridge Lane.
- Chlorinated the line and sent a sample out for testing. (Line not tie-in at this time).

CALICO LANE

- This period no work was performed on this aspect of the project.
- This period no work was performed on this aspect of the project.

GINGHAM DRIVE

- None required

GREEN OAK DRIVE/HABERSHAM
DITCH OUTFALL

- None required

TREE PROTECTION:

JAMESTOWN ROAD

- This period no work was performed on this aspect of the project.

January 19, 2014 to January 25, 2014
Activity/Status

Batch # 1 Paving & Drainage
IMPROVEMENTS

TREE PROTECTION: (cont.)

CALICO LANE

- This period no work was performed on this aspect of the project.

JAN KELLY LANE

- This period no work was performed on this aspect of the project at this time

GINGHAM DRIVE

- This period no work was performed on this aspect of the project.



Contractor installing the new storm line on the north end of Gingham. View to the north.

[January 19, 2014 to January 25, 2014
Activity/Status](#)

**Batch # 1 Paving & Drainage
IMPROVEMENTS**

**GREEN OAK DRIVE/HABERSHAM
DITCH OUTFALL**

- Completed

SUPPLEMENTAL ITEMS:

JAMESTOWN ROAD

- This period no work was performed on this aspect of the project.

CALICO LANE

- This period no work was performed on this aspect of the project.

JAN KELLY LANE

- This period no work was performed on this aspect of the project.

GINGHAM DRIVE

- Removed the old stump ground material from the back yard of 430 Gingham Dr.

**GREEN OAK DRIVE/HABERSHAM
DITCH OUTFALL**

- Completed

[January 19, 2014 to January 25, 2014
Activity/Status](#)

**Batch # 1 Paving & Drainage
IMPROVEMENTS**



Excavating for the water line off set on Tynebridge Lane View to the north.




The contractor placed more sod grass in the easement between 426 and 430 Gingham Dr. View to the east.

Next Week's Planned Activities
January 26, 2014 to February 1, 2014

Batch # 1 Paving & Drainage
IMPROVEMENTS

MOBILIZATION:

- This period no work was performed on this aspect of the project.

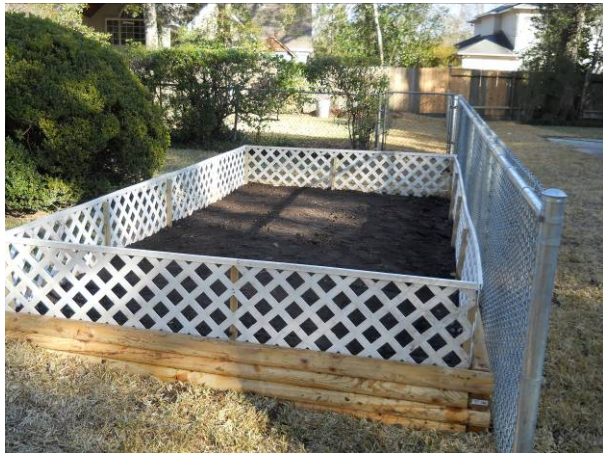

Contractor replaced the garden fencing in the easement between 426 and 430 Gingham Dr. View to the east.

PAVING ITEMS: AAA Paving

JAMESTOWN ROAD

- This period no work was is planned on this aspect of the project.

CALICO LANE

- This period no work is planned on this aspect of the project.

JAN KELLY LANE

- This period no work is planned on this aspect of the project.

GINGHAM DRIVE

- This period no work is planned on this aspect of the project.

Next Week's Planned Activities
January 26, 2014 to February 1, 2014

Batch # 1 Paving & Drainage
IMPROVEMENTS

GREEN OAK DRIVE

- This period no work is planned on this aspect of the project.

DRAINAGE ITEMS: AAA Paving

JAMESTOWN ROAD

- This period no work is planned on this aspect of the project.

CALICO LANE

- Continue placement of the new 24-inch storm sewer line.



Contractor placed the sod grass and repaired the gate at 430 Gingham Dr, View to the east.

JAN KELLY LANE

- This period no work is planned on this aspect of the project.

Next Week's Planned Activities (cont.)
January 26, 2014 to February 1, 2014

Batch # 1 Paving & Drainage
IMPROVEMENTS

DRAINAGE ITEMS: AAA Paving (cont.)

GINGHAM DRIVE

- Complete the installation of the storm sewer pipe and inlets.
- Reconnect the yard drains.
- Remove the old inlets and storm sewer piping.

GREEN OAK DRIVE/HABERSHAM
DITCH OUTFALL

- Completed

WATER ITEMS:

JAMESTOWN ROAD

- Install the by-pass water line on Tynebridge Lane.

CALICO LANE

- This period no work is planned on this aspect of the project.

JAN KELLY LANE

- Completed

GINGHAM DRIVE

- This period no work is planned on this aspect of the project.

GREEN OAK DRIVE/HABERSHAM
DITCH OUTFALL

- This period no work is planned on this aspect of the project.

Next Week's Planned Activities (cont.)
January 26, 2014 to February 1, 2014

Batch # 1 Paving & Drainage
IMPROVEMENTS

TREE PROTECTION:

JAMESTOWN ROAD

- Initiated the root pruning, tree pruning and tree removal.

CALICO LANE

- This period no work is planned on this aspect of the project.

JAN KELLY LANE

- This period no work is planned on this aspect of the project.

GINGHAM DRIVE

- This period no work is planned on this aspect of the project.

TREE PROTECTION: (cont.)

GREEN OAK DRIVE/HABERSHAM
DITCH OUTFALL

- This period no work is planned on this aspect of the project.

SUPPLEMENTAL ITEMS:

JAMESTOWN ROAD

- This period no work is planned on this aspect of the project.

CALICO LANE

- This period no work is planned on this aspect of the project.

[Next Week's Planned Activities \(cont.\)](#)
[January 26, 2014 to February 1, 2014](#)

Batch # 1 Paving & Drainage
IMPROVEMENTS

SUPPLEMENTAL ITEMS: (cont.)

JAN KELLY LANE

- This period no work is planned on this aspect of the project.

GINGHAM DRIVE

- This period no work is planned on this aspect of the project.

GREEN OAK DRIVE/HABERSHAM
DITCH OUTFALL

- This period no work is planned on this aspect of the project.



Contractor had dressed up the sides of Jan Kelly. Home contractors worker parked on the dress up area of Jan Kelly leaving ruts. View to the south



The yard drain was installed on the back side of a fire hydrant because of the FH valve. View to the southwest.



The contractor had dressed up and cut to grade the sides of Gingham when the water crew on Bending Oaks and a tree trimming truck drove over and parked on the area. View to the east.
